

Pricing & Timeline


SDLC Delivery Plan — Design + Development Phases

Version 1.3 | **Date** June 27, 2026 | **Confidential**

© 2026 GlowTap

1. Executive Summary

GlowTap delivery follows a **strict three-phase sequence**. Each phase gates the next stage of work:

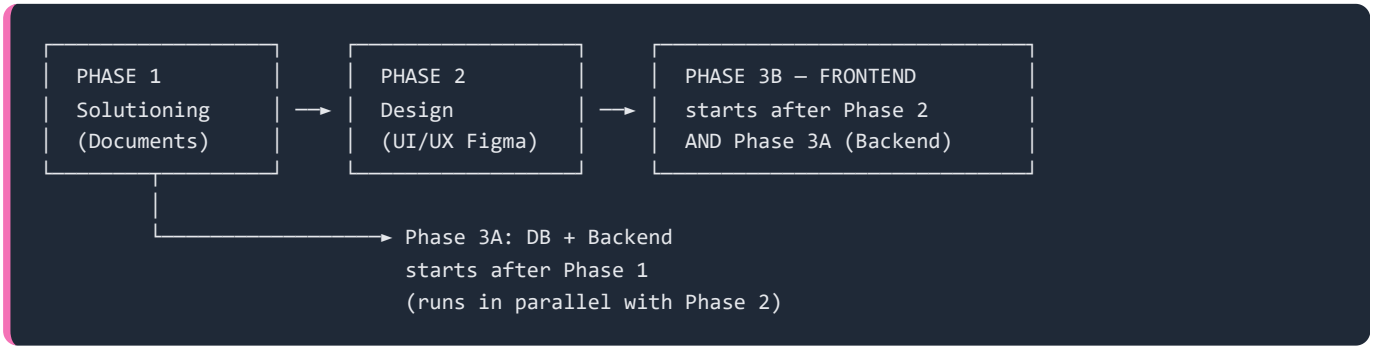

Phase	Order	Scope	Investment
Phase 1 — Solutioning	**1st**	Functional + Solutioning documents (all portals)	Part of **₹2,30,000** (M1, M2)
Phase 2 — Design	**2nd**	UI/UX screen designs (Super Admin, Admin, Customer)	**₹60,000**
Phase 3 — Development	**3rd**	DB architecture, backend APIs, frontend (React)	Part of **₹2,30,000** (M3–M5)
Grand Total			**₹2,90,000**

Phase Gate Rules


Gate	Rule
Design (Phase 2)	Starts **after Phase 1 (Solutioning)** — designs are based on approved functional & solution specs
DB + Backend (Phase 3A)	Starts **after Phase 1 (Solutioning)** — schema and APIs derived from approved solution documents
Frontend (Phase 3B)	Starts **after Phase 2 (Design) closure AND Phase 3A (Backend) closure** — 20 working days; Super Admin + Admin React only

> **Note:** Backend and Design may **run in parallel** once solutioning is complete. **Frontend starts only after both Design sign-off and Backend closure** (all APIs available via Swagger).

> End Customer **React Native** app development is **out of scope** for Phase 3 frontend. Customer **APIs** and **UI designs** are included.

2. SDLC Overview

SDLC Phase	GlowTap Deliverable	Project Phase	Target
Planning & Requirements	Kickoff, scope agreement, sample screen review	Pre-Phase 2	June 29, 2026
Analysis & Solutioning	Functional + Solutioning PDFs (all portals)	**Phase 1**	See §3
Design	Figma screen designs (first drafts + iterations)	**Phase 2**	See §4
Architecture	DB schema, system architecture, infra sizing	**Phase 3** (post-Phase 1)	July 20–25, 2026
Development — Backend	Interlinked microservices + Swagger	**Phase 3** (post-Phase 1)	End of August, 2026
Development — Frontend	React web — Super Admin + Admin	**Phase 3B** (post-Phase 2 + 3A)	20 days after design **and** backend closure
Testing	Unit tests, DB performance report (PL/SQL)	Phase 3	With M3–M5
Deployment	AWS EC2 production handover	Phase 3	Post frontend
Maintenance	Post-go-live support	—	Separate agreement

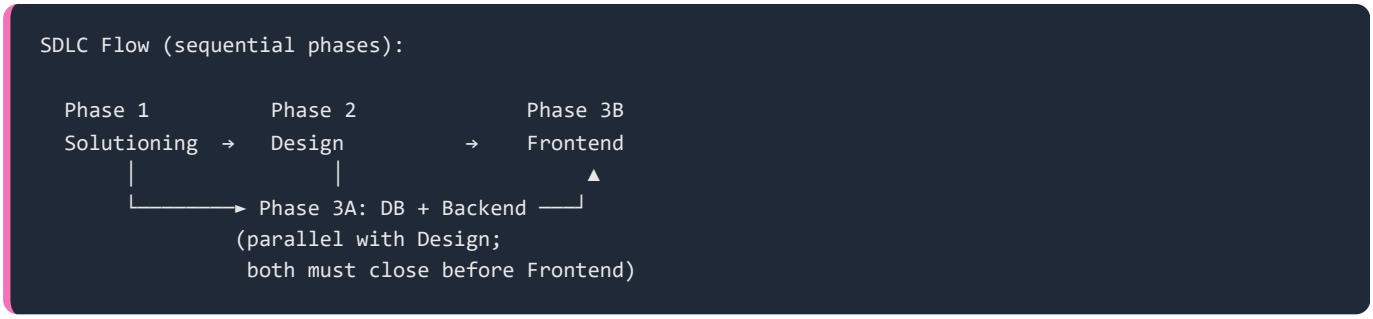

3. Phase 1 — Solutioning *(First)*

3.1 Objective

Define **what** the platform does and **how** it will be built — functional specifications and technical solutioning documents for all three portals **before** design or development begins.

3.2 Solution Documentation Timeline

Document / Portal	Status	Target Date
Super Admin — Functional + Solutioning	**Closed & Approved**	Complete
Salon Admin — Functional + Solutioning	In progress	**July 1, 2026**
End Customer — Functional + Solutioning	In progress	**July 5, 2026**

3.3 Phase 1 Deliverables

- Functional Specification PDF (business flows, modules, rules)
- Solutioning & Technical Architecture PDF (stack, data model, APIs, deployment)
- Stakeholder review and written approval per portal
- Baseline for Phase 2 (Design) and Phase 3 (DB / Backend)

3.4 Phase 1 — Pricing & Payment Milestones

Milestone	Description	Amount	Cumulative
M1 — Advance Payment	Project kickoff	**₹20,000**	₹20,000
M2 — Solutioning & Functional Document Closure	All three portal specs approved (Super Admin ✓, Admin, Customer)	**₹20,000**	**₹40,000**

Phase 1 subtotal (within development engagement): ₹40,000

> Phase 1 closure (all solution docs approved by **July 5, 2026**) **unlocks** Phase 2 (Design kickoff) and Phase 3 DB/Backend work.

4. Phase 2 — Design *(Second)*

4.1 Objective

Deliver **first-draft UI/UX screen designs** in Figma for all three portals — **after** solutioning documents are approved. Designs reflect approved functional flows, brand identity (logo, purple/violet theme), and mobile-first beauty-tech positioning.

4.2 Pre-Requisite

Requirement	Date	Impact if Delayed
Phase 1 complete — solution docs approved	**By July 5, 2026**	Blocks design kickoff
Stakeholder confirmation of **sample screens**	**June 29, 2026**	Shifts all design dates below

4.3 Design Timeline (First Drafts)

Portal	First Draft Target	Payment Trigger
Super Admin screens	**July 10, 2026**	D2 milestone
Salon Admin portal	**July 25, 2026**	D3 milestone
End Customer screens	**August 10, 2026**	D4 milestone

> First drafts only. Final closure driven by feedback cycles. Delays in sample confirmation or feedback shift dates proportionally.

4.4 Design Feedback SLA

Priority	Definition	Turnaround
Critical	Blocker — impacts dependent screens or delivery dates	**2 business days**
High	Blocker for a screen but not overall schedule	**3 business days**
Low	Cosmetic / non-blocking changes	**5 business days**

4.5 Design Scope & Exclusions

Included: Screen designs (3 portals), logo/brand integration, iteration per SLA, Figma exports (free tier).

Excluded: Figma paid plan costs (reimbursed on actuals if required), React Native build, advanced prototypes (unless CR).

4.6 Phase 2 — Pricing & Payment Milestones

Milestone	Description	Amount	Cumulative
D1 — Advance	Design kickoff (post-Phase 1)	**₹10,000**	₹10,000
D2 — Super Admin Screen Closure	Super Admin designs approved	**₹15,000**	₹25,000
D3 — Admin Portal Design	Salon Admin designs accepted	**₹20,000**	₹45,000
D4 — Customer Screen Design	Customer designs accepted	**₹15,000**	**₹60,000**

Phase 2 Total: ₹60,000

> Revised from ₹40,000 to **₹60,000** for complexity, logo integration, and iteration volume.

> **Phase 2 full closure (D4)** is required for frontend. **Phase 3A backend closure** is also required. Frontend kickoff occurs when **both** are complete.

---

5. Phase 3 — Development *(Third)*

5.1 Objective

Build production-ready **database**, **backend microservices**, and **React frontend** per approved solutioning (Phase 1) and design (Phase 2).

5.2 Technology Stack

Layer	Technology
Frontend (Web)	React + TypeScript, Redux Toolkit + RTK Query
Frontend (Mobile)	React Native *(out of scope for dev milestone)*
Backend	Node.js + Fastify (TypeScript)
Database	PostgreSQL or MongoDB *(TBD)*
Cache	Redis / Valkey
Storage	AWS S3
Jobs	BullMQ
Deployment	AWS EC2
API Docs	Swagger (OpenAPI)

5.3 Track A — DB & Backend *(Starts after Phase 1)*

Begins once solutioning documents are approved. May **run in parallel** with Phase 2 (Design).

Database & Architecture + Performance Testing

Deliverable	Target Date
Database schema	**July 20–25, 2026**
System architecture document	**July 20–25, 2026**
Performance testing report (PL/SQL)	**July 20–25, 2026**

Performance test environment:

Resource	Specification
vCPU	8 Cores
RAM	32 GB
Disk	400 GB NVMe
Bandwidth	32 TB

Backend Microservices


Interlinked services — planned closure **End of August 2026**.

Module	Swagger	Milestone Value
Super Admin APIs	Yes	₹20,000
Salon Admin APIs	Yes	₹20,000
Customer APIs	Yes	₹40,000

Per module: REST endpoints, Swagger docs, unit tests, shared service integration (auth, DB, Redis, S3, BullMQ).

5.4 Track B — Frontend *(Starts after Phase 2 + Phase 3A)*

Item	Detail
Start condition	**Both** gates satisfied: (1) Phase 2 (Design) fully closed — D4 sign-off, **AND** (2) Phase 3A (Backend) closed — all APIs live with Swagger (end Aug)
Duration	**20 working days** from dual-closure date
In scope	Super Admin + Salon Admin React web portals
Out of scope	End Customer React Native app
Estimated start	~Early September, 2026 *(design ~August 10 + backend end of August)*
Estimated completion	~Late September / Early October 2026

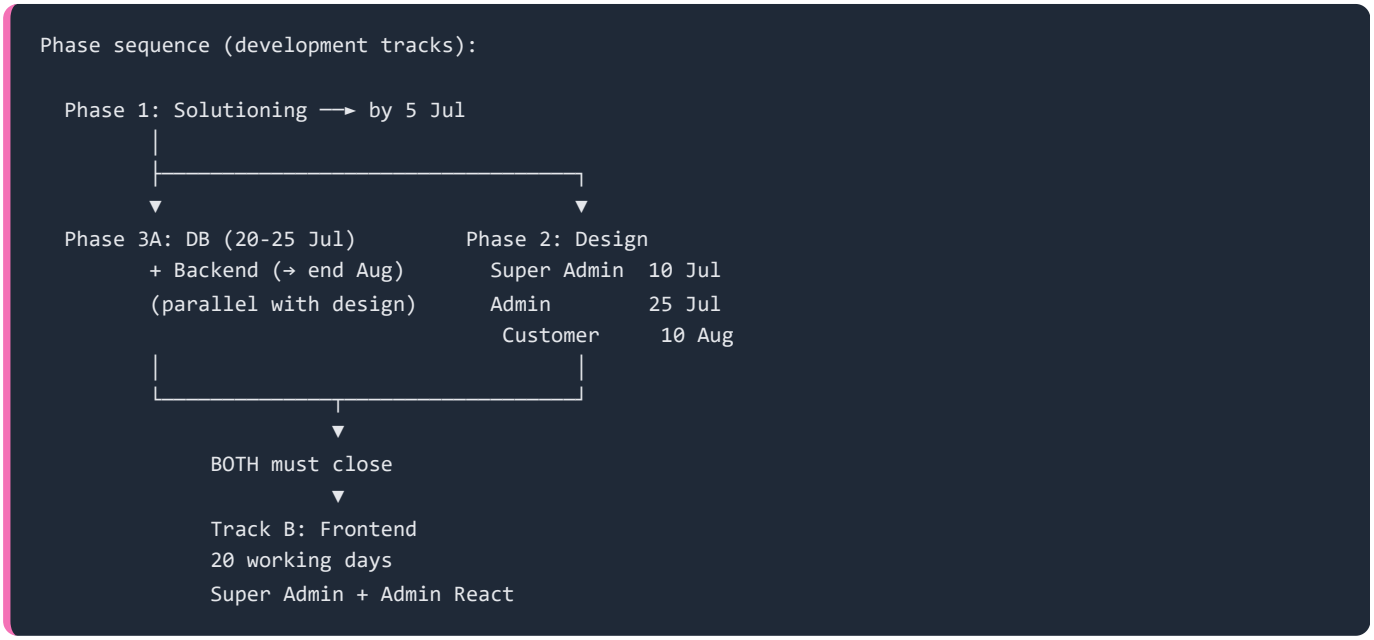

5.5 Testing & Deployment

Activity	When	Deliverable
DB performance testing	July, 2026 (M3)	Benchmark report
Backend unit tests	August, 2026 (M4)	Test suites per service
API integration testing	August, 2026	Swagger coverage
Frontend testing	Post 20-day sprint	React component + integration tests
UAT	Pre-deployment	Staging on EC2
Deployment	Post frontend	Production handover, runbook, repo access

5.6 Phase 3 — Pricing & Payment Milestones

Milestone	Description	Amount	Cumulative (Phase 3)
M3 — DB Architecture & Performance Report	Schema, architecture, PL/SQL perf report	**₹30,000**	₹30,000
M4 — Backend + Unit Tests	All microservices + Swagger	**₹80,000**	₹1,10,000
M5 — Frontend (React Only)	Super Admin + Admin portals; Cursor included	**₹80,000**	**₹1,90,000**

Phase 3 subtotal: ₹1,90,000
Phase 1 + Phase 3 combined: ₹2,30,000

M4 Breakdown (Backend)

Module	Amount
Super Admin APIs + Swagger	₹20,000
Admin APIs + Swagger	₹20,000
Customer APIs + Swagger	₹40,000

© 2026 GlowTap

Confidential

M5 Breakdown (Frontend)

Module	Amount
Super Admin — React	₹40,000
Salon Admin — React	₹40,000
Cursor usage	Included

6. Combined Pricing Summary

Phase	Order	Total
Phase 1 — Solutioning	1st	₹40,000 *(M1 + M2)*
Phase 2 — Design	2nd	₹60,000 *(D1–D4)*
Phase 3 — Development	3rd	₹1,90,000 *(M3–M5)*
Grand Total		**₹2,90,000**

Payment Schedule (Chronological)

#	Phase	Milestone	Amount	Trigger
1	1	M1 — Advance	₹20,000	On signing
2	2	D1 — Design advance	₹10,000	After Phase 1 kickoff / design start
3	1	M2 — Solution docs closure	₹20,000	Admin (July 1) + Customer (July 5) approved
4	2	D2 — Super Admin designs	₹15,000	Super Admin screens — July 10
5	3	M3 — DB + Architecture + Perf	₹30,000	July 20–25 accepted
6	2	D3 — Admin designs	₹20,000	Admin portal — July 25
7	3	M4 — Backend + unit tests	₹80,000	End of August — APIs + Swagger
8	2	D4 — Customer designs	₹15,000	Customer screens — August 10
9	3	M5 — Frontend (React)	₹80,000	20-day sprint complete (post design + backend closure)

© 2026 GlowTap

Confidential

```
Phase 1  Solutioning   ₹20K ⟶ ₹20K                    = ₹40,000
Phase 2  Design        ₹10K ⟶ ₹15K ⟶ ₹20K ⟶ ₹15K = ₹60,000
Phase 3  Development            ₹30K ⟶ ₹80K ⟶ ₹80K = ₹1,90,000
         ──────────────────────────────────────────────────────
         Grand Total                                  ₹2,90,000
```

7. Master Timeline (Gantt View)

Activity	Jun	Jul	Aug	Sep	Oct
PHASE 1 Sample screens confirm (June 29)	◆				
PHASE 1 Super Admin solution docs	✓				
PHASE 1 Admin + Customer solution docs		◆◆			
PHASE 3A DB + Architecture + Perf (July 20–25)		◆			
PHASE 3A Backend microservices (→ end Aug)		▓▓▓▓▓▓	▓▓▓▓		
PHASE 2 Super Admin designs (July 10)		◆			
PHASE 2 Admin designs (July 25)		◆			
PHASE 2 Customer designs (August 10)			◆		
PHASE 3B Frontend React — 20 days (post design + backend)				▓▓▓▓	◆
Deployment & handover				◆	

Legend: ✓ Done | ◆ Milestone | ▓▓▓▓ Active work

Note: Phase 3A (DB/Backend) runs **parallel** to Phase 2 (Design) after Phase 1 closes.

8. Assumptions & Dependencies

Stakeholder

- Confirm sample screens by **June 29, 2026**
- Approve solution docs within **5 business days** of submission
- Provide feedback per design SLA (§4.4)
- Designate single point of contact

Delivery Team

- Complete Phase 1 before Phase 2 kickoff
- Start DB/Backend immediately after Phase 1 approval
- Start Frontend only after **Phase 2 (D4) and Phase 3A (backend)** both signed off
- Weekly status updates during active sprints

Key Assumptions

- Phase order: **Solutioning → Design**; **Backend post-Solutioning**; **Frontend post-Design AND post-Backend**
- DB selection finalized before M3 (target: July 15, 2026)
- Scope per approved specs; additions are change requests
- Customer React Native quoted separately if needed

9. Change Request Policy

Out-of-scope changes documented within 3 business days, executed on written approval only.

Change Type	Impact
New API module	Backend timeline + cost
Design rework post sign-off	Design extension + quote
Customer mobile app	Separate SOW

10. Risk Register

Risk	Mitigation
Phase 1 delay past July 5	Blocks Phase 2 and Phase 3A start — recalculate all dates
Sample screens not confirmed (June 29)	Escalate; shifts Phase 2 dates
Design started before solutioning	**Not permitted** — enforce phase gate
Frontend started before design or backend closure	**Not permitted** — dual gate enforced
Design or backend lag near frontend start	Confirm dual-closure date in writing before M5 kickoff
Figma free tier limits	Reimburse paid plan on actuals

© 2026 GlowTap

Confidential

11. Acceptance Criteria

Phase 1 — Solutioning

- [ ] Functional + Solutioning PDFs delivered per portal
- [ ] Written stakeholder approval

Phase 2 — Design

- [ ] Figma screens per portal with brand theme
- [ ] Written sign-off or feedback log per D2–D4

Phase 3 — Development

Milestone	Criteria
M3	ER diagram, schema, architecture doc, perf report
M4	Swagger live; unit tests pass; core flows operational
M5	Super Admin + Admin React on staging, API-connected

12. Out of Scope

- End Customer React Native development
- Figma paid fees (reimbursed if required)
- AWS running costs, payment gateway setup, app store submission
- Post-warranty maintenance, content creation

13. Document Control

Version	Date	Changes
1.3	June 27, 2026	Added §14 Delivery Delay Tracker
1.2	June 27, 2026	Frontend gate: requires both Design closure and Backend closure
1.1	June 27, 2026	Reordered phases: Solutioning 1st → Design 2nd → Dev tracks
1.0	June 27, 2026	Initial release

© 2026 GlowTap

Confidential

14. Delivery Delay Tracker

Use this section to record **actual vs planned delivery dates**, delay duration, root cause, and agreed recovery actions. Update after each phase or milestone review.

14.1 Phase 1 — Solutioning

Deliverable	Planned Date	Actual Date	Delay (Days)	Reason	Owner	Recovery / Revised Date
Super Admin — Functional + Solutioning	Complete		—			
Salon Admin — Functional + Solutioning	July 1, 2026					
End Customer — Functional + Solutioning	July 5, 2026					
M2 — Phase 1 closure (all docs approved)	July 5, 2026					

14.2 Phase 2 — Design

Deliverable	Planned Date	Actual Date	Delay (Days)	Reason	Owner	Recovery / Revised Date
Sample screens — stakeholder confirmation	June 29, 2026					
Super Admin — first draft (D2)	July 10, 2026					
Salon Admin — first draft (D3)	July 25, 2026					
End Customer — first draft (D4)	August 10, 2026					
Phase 2 closure (all designs signed off)	August 10, 2026					

© 2026 GlowTap

Confidential

14.3 Phase 3A — DB & Backend

Deliverable	Planned Date	Actual Date	Delay (Days)	Reason	Owner	Recovery / Revised Date
DB schema + architecture document	July 20–25, 2026					
Performance testing report (PL/SQL)	July 20–25, 2026					
M3 — DB + Architecture + Perf report accepted	July 25, 2026					
Super Admin APIs + Swagger	End of August, 2026					
Salon Admin APIs + Swagger	End of August, 2026					
Customer APIs + Swagger	End of August, 2026					
M4 — Backend closure (all APIs + unit tests)	End of August, 2026					

14.4 Phase 3B — Frontend

Deliverable	Planned Date	Actual Date	Delay (Days)	Reason	Owner	Recovery / Revised Date
Dual gate met (Design D4 + Backend M4)	End of August, 2026					
Frontend sprint start (Super Admin + Admin React)	TBD post dual gate					
M5 — Frontend closure (20 working days)	TBD + 20 days					
Deployment & handover (EC2 staging/prod)	Post M5					

© 2026 GlowTap

Confidential

14.5 Delay Summary Log

#	Date Logged	Phase / Milestone	Days Delayed	Category	Reason (summary)	Impact	Action Taken
1				Stakeholder / Delivery / Technical / Scope			
2							
3							

Delay categories:

Category	Examples
Stakeholder	Late feedback, sample screen confirmation slip, approval delays
Delivery	Resource availability, dependency on third-party access
Technical	DB selection pending, infra provisioning, integration blockers
Scope	Change requests, new requirements post sign-off

> **Review cadence:** Update this tracker at each milestone payment trigger and in weekly status meetings. Revised dates in the Recovery column supersede planned dates in §3–§5 until the next change.

---

*Phase 1 must complete before Phase 2 begins. Phase 3A (Backend) may start after Phase 1 and run parallel to Phase 2. Phase 3B (Frontend) starts only after **both** Phase 2 and Phase 3A close.*

© 2026 GlowTap

Confidential
